

# **Smithtown Central School District**

**Athletic Field Renovations HS West**

**Fieldhouse Additions HS East & West**

**Fire Alarm Reconstruction HS West**

**Project Briefing : February 2023**

## **Board of Education Update**

**March 6, 2023**

# Table of Contents

- a. Project Briefing
- b. Progress Photographs

**Project Briefing March 6, 2022**  
**Smithtown Central School District**

**Work completed in February 2023**



**Smithtown High School West Athletic Field Renovations**  
**Varsity Softball Field & Varsity Baseball Field**

- **Awaiting final turnover to district prior**

## Smithtown High School East & West Field Houses



- Start and complete concrete flatwork and walkways
- Complete septic system and backfill (except formal startup)
- Start and complete roofing at West, start and continue roofing at East
- Prepare site for asphalt installation
- Start drywall ceilings (West)
- Upcoming work:
  - Weather permitting – Asphalt installation, soffit completion, start finishes, start flooring (West, weather permitting)

**Smithtown High School West Final 100 13.2.11A**


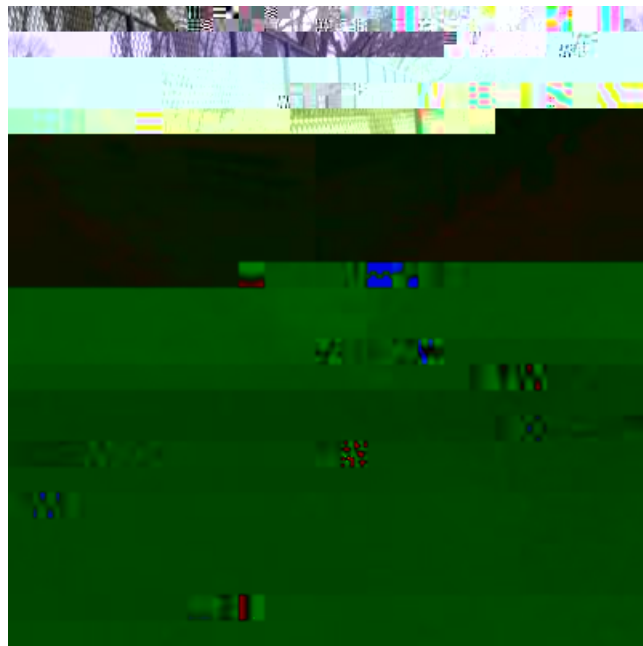
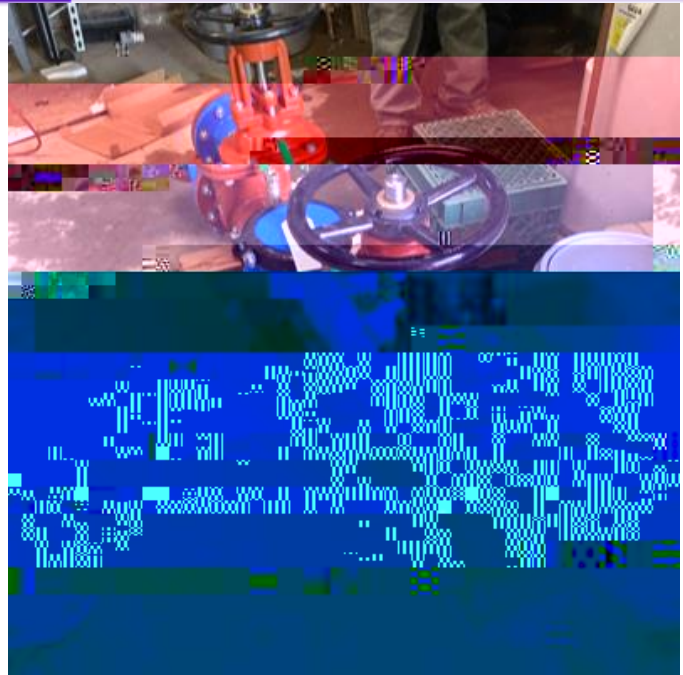


East Field House – Complete septic system and backfill, install new RPZ, install underground electric for bollard lighting



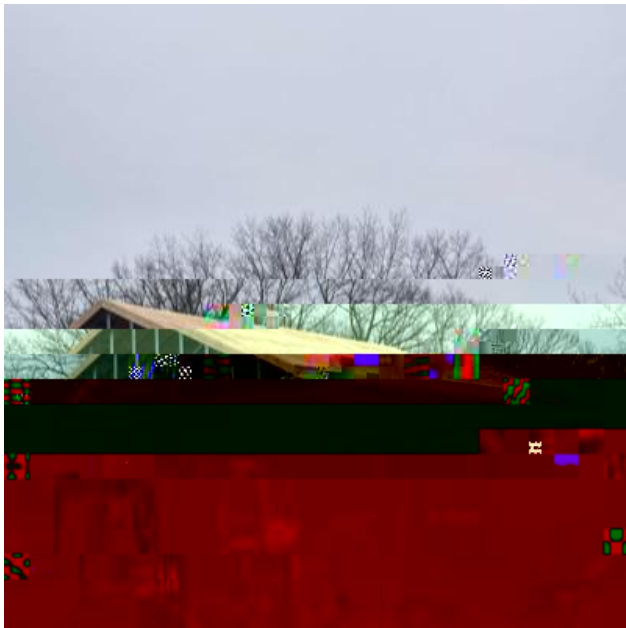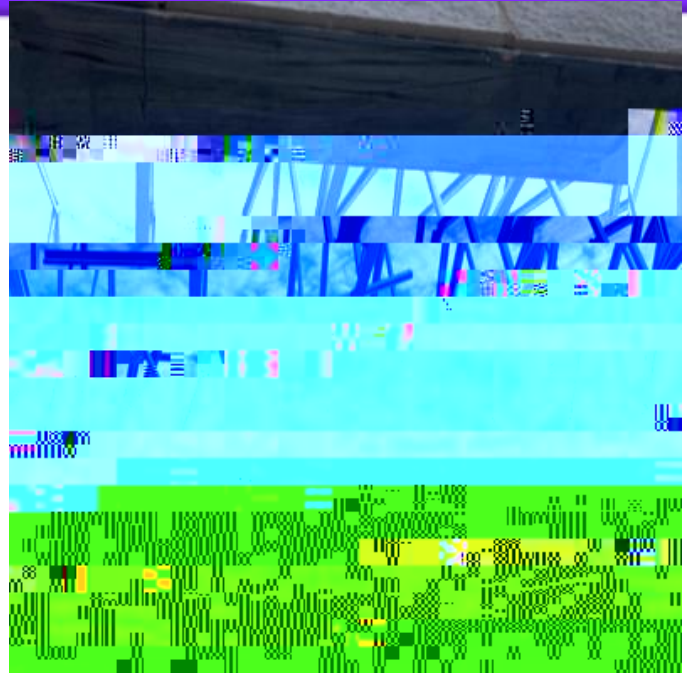

West Field House – Complete masonry, start and complete roof, finish septic system and backfill

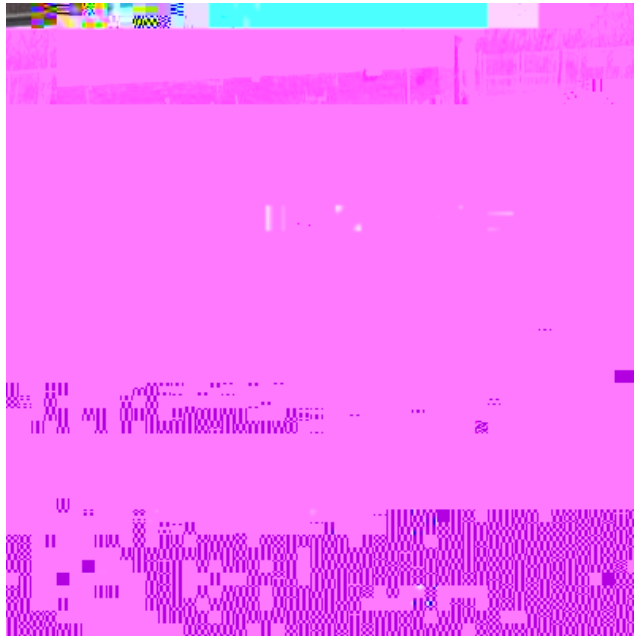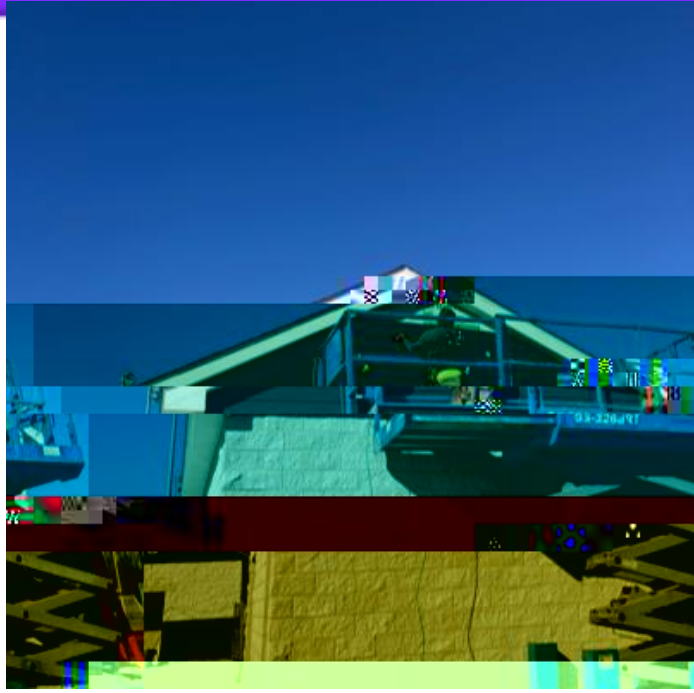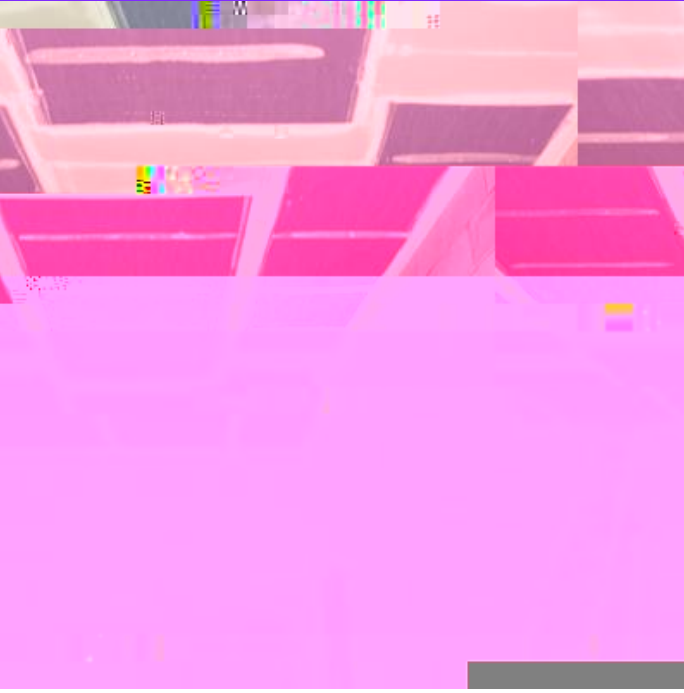

West Field House – Start and complete drywall ceilings, complete siding, prep subbase for asphalt,
